


Table 5-4.2 Dispute Resolution Board Process

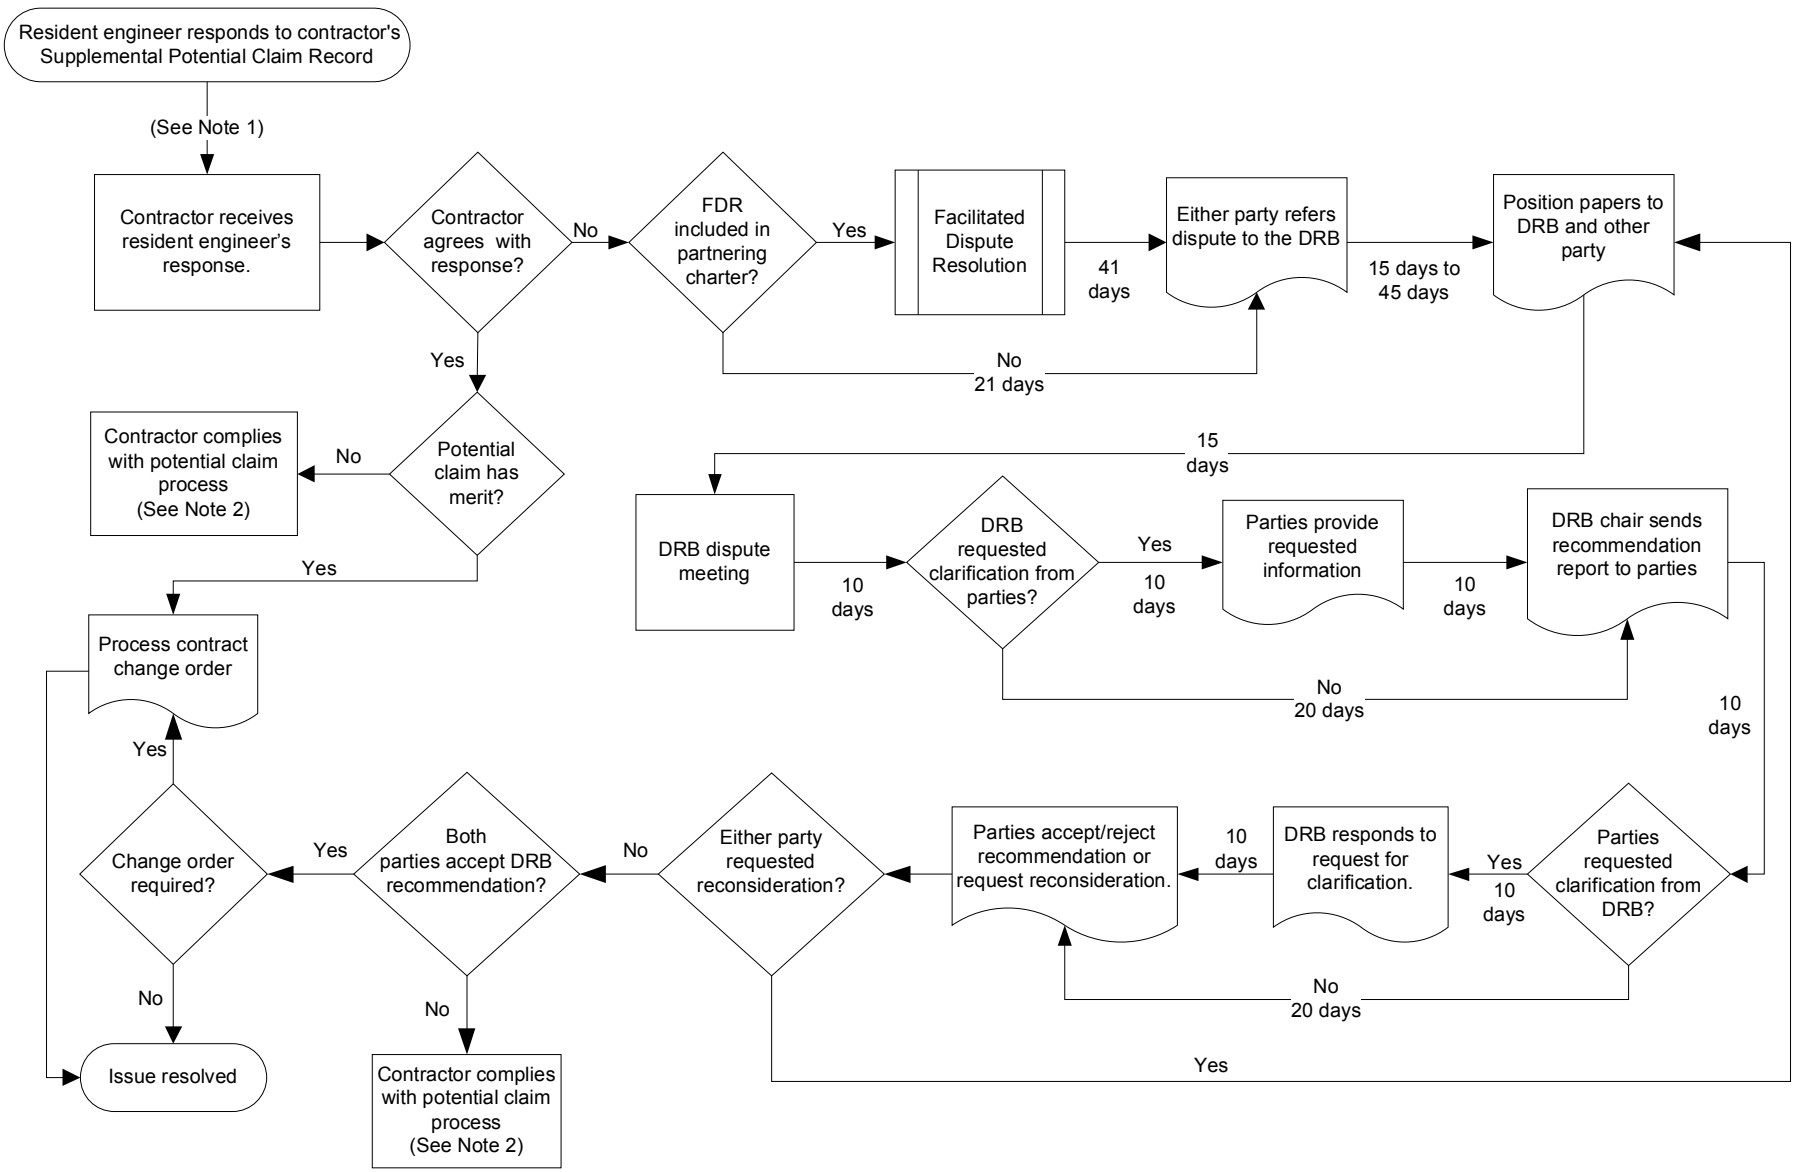

Notes:

1. The dispute resolution board process begins upon the contractor's receipt of the resident engineer's response to the Supplemental Potential Claim Record. The resident engineer should respond to the supplemental potential claim record as quickly as possible not to exceed 20 days.

2. For the Potential Claim Process flow chart, refer to Table 5-4.1 Request for Information and Potential Claim Process.

DRB = Dispute Resolution Board

FDR = Facilitated Dispute Resolution
